


# GREENVALE WEEKLY UPDATE (6/21/21 to 6/25/21)



## Greenvale Improvements Updates:

- On June 21st – The Contractor, All-Ways, installed new 36” HDPE storm sewer up to Greenvale Road.
- On June 22nd – All-Ways connected new storm sewer to existing storm sewer in a new manhole by Greenvale Road.
- On June 23rd – All-Ways installed storm sewer from the outlet structure of the proposed pond to the existing concrete channel.
- On June 24th – All-Ways installed storm sewer across Greenvale road that will connect the existing pond to the proposed pond.
- On June 25th – No work was performed due to rain making the site to wet to work on.

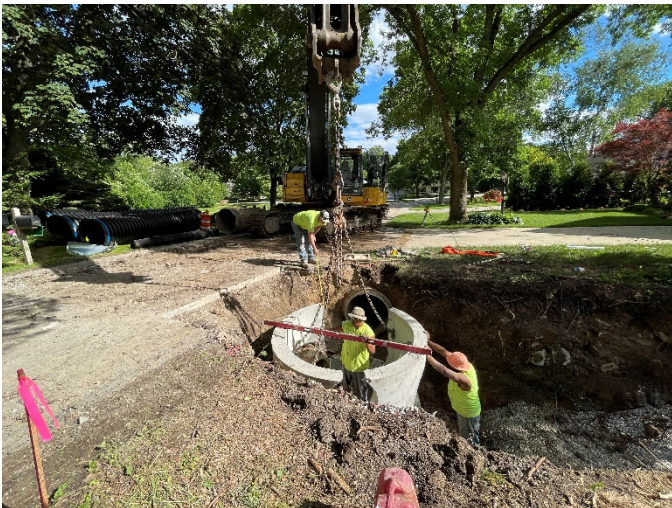

## A Look Forward: Week of June 28th

- The Contractor, All-Ways, will let the site dry out with the rain from last week and will not be on site to begin the week.
- All-Ways will watch the weather but with more rain in the forecast, it might push their work back a few more days.

